


TOTAL DE FALTANTE

- 3 LUCES
- 8 VENTILADORES
- 4 TOMAS
- 1 A/A DE 12 MIL BTU POR AULAS

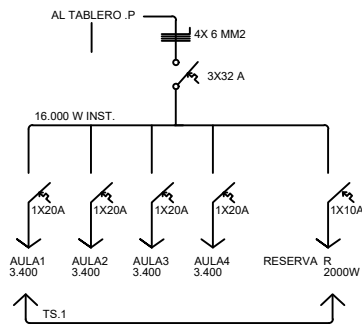

TS.8 (5 AULAS -- INCLUYE ESCALERA Y BIBLITECA)
 LUC TC VT A/A WAT

AULA 1	6	2	4	1.200	2.000	3.200
AULA 2	6	2	4	1.200	2.000	3.200
AULA 3	6	2	4	1.200	2.000	3.200
AULA 4	6	2	4	1.200	2.000	3.200
BBLI T	6	2	4	1.200	2.000	3.200

REAL :16.000-----16.000

OBS. -- SE DEBERA COMPLETAR CON ESTAS CANTIDADES
 QUEDANDO ASI 4+2 GAL . LAMAPARAS ACRILICAS P/ CADA AULA

- 4 VENTILADORES POR AULAS ,
- 4 TOMAS POR AULAS ,
- 1 A/A DE 12 MIL BTU POR AULAS

TABLEROS DE 18 MODULOS

- 5 TM DE 1X10 A
- 4 TM DE 1X 16 A
- 4 TM DE 1 X 20 A
- 1 DE 3X32 A..

